

NEEDVILLE

INDEPENDENT SCHOOL DISTRICT

WE APPRECIATE
THE OPPORTUNITY TO SERVE YOU!
THANK YOU!



NEW JUNIOR HIGH PROJECT UPDATE

Last Month:

- Installed flooring throughout the academic hallways and classrooms.
- Install interior doors throughout the building.
- Installed bleachers in the competition gym.
- Pouring concrete sidewalk and canopies around the exterior of the building.
- Installing the athletics turf on the athletic field.

Next Month:

- Continue installation of flooring throughout the building.
- Continue dropping ceiling grid in the Athletic and common areas.
- Continue the rough in for electrical outlets and light switches.
- Kitchen equipment is being installed.
- Field bleacher foundation is being prepared.



NEEDVILLE ISD

NEEDVILLE NEW JUNIOR HIGH SCHOOL



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW JUNIOR HIGH SCHOOL PROJECT UPDATE



NEEDVILLE ISD
NEEDVILLE JUNIOR HIGH



NEW ELEMENTARY SCHOOL PROJECT UPDATE

Current Schedule:

11/03/2025: Issue Bid Documents

12/03/2025: Drymalla Received Bids

01/28/2026: Establish GMP for approval

02/18/2026: Ground Breaking Ceremony

06/01/2027: Complete Construction



NEEDVILLE ISD

NEEDVILLE NEW ELEMENTARY SCHOOL



NEW ELEMENTARY SCHOOL PROJECT UPDATE

Last Month:

- GROUND BREAKING!
- Clear cut the land.
- Bringing select fill to raise the building pad.

Next Month:

- Continue building the building pad.
- Continue dirt work around the building and excavating the detention pond.
- Utility material to began being brought to the site
- Secure the site and add additional cameras.
- Begin bringing concrete accessories and rebar to the site.



NEEDVILLE ISD

NEEDVILLE NEW ELEMENTARY SCHOOL



NEW ELEMENTARY SCHOOL PROJECT UPDATE



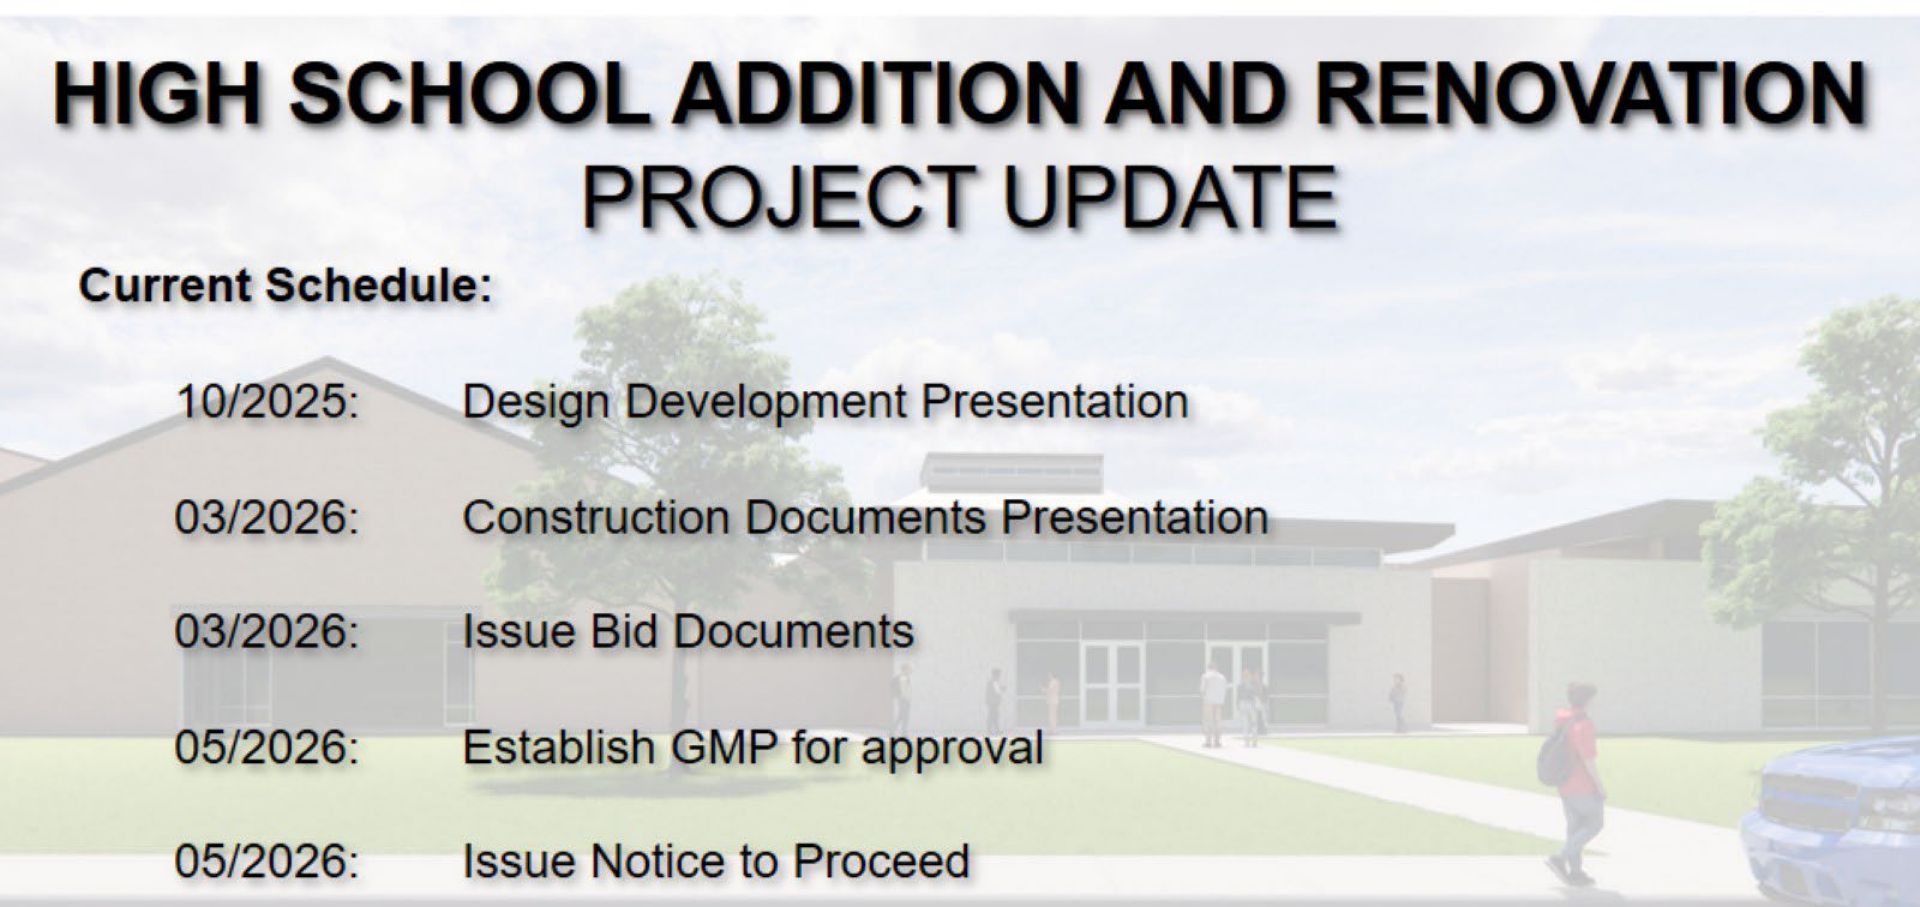
NEEDVILLE ISD

NEEDVILLE NEW ELEMENTARY SCHOOL



HIGH SCHOOL ADDITION AND RENOVATION PROJECT UPDATE

Current Schedule:

- 
- 10/2025: Design Development Presentation
 - 03/2026: Construction Documents Presentation
 - 03/2026: Issue Bid Documents
 - 05/2026: Establish GMP for approval
 - 05/2026: Issue Notice to Proceed
 - 08/2027: Complete Construction



NEEDVILLE ISD

NEEDVILLE HIGH SCHOOL ADDITION AND RENOVATION



NEEDVILLE

INDEPENDENT SCHOOL DISTRICT

WE APPRECIATE
THE OPPORTUNITY TO SERVE YOU!
THANK YOU!



Designing Schools . . . With Kids in Mind!

www.claycomb.net
