## NEEDVILLE

INDEPENDENT SCHOOL DISTRICT

# WE APPRECIATE THE OPPORTUNITY TO SERVE YOU! THANK YOU!













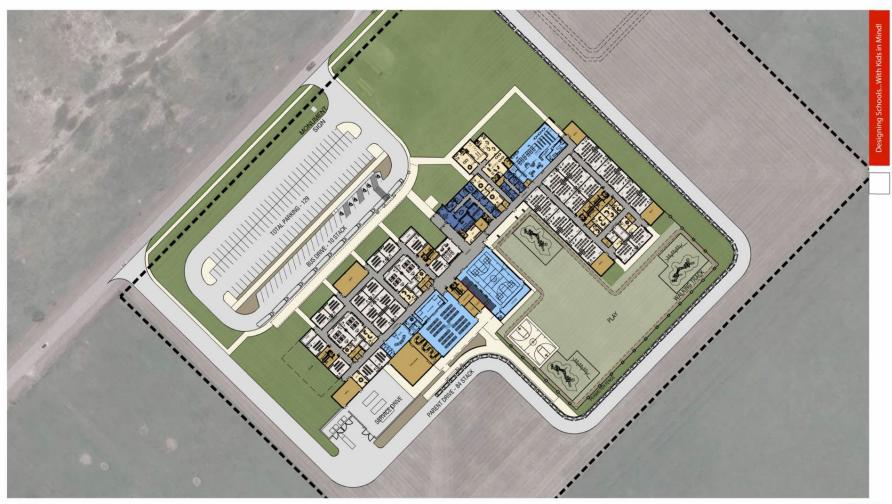









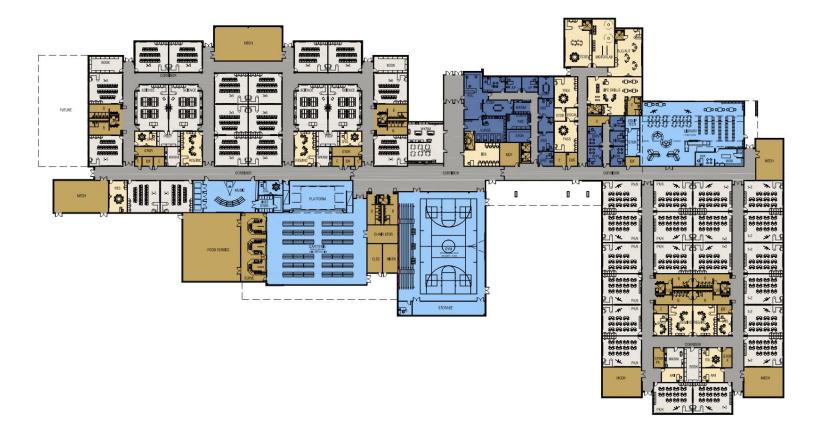







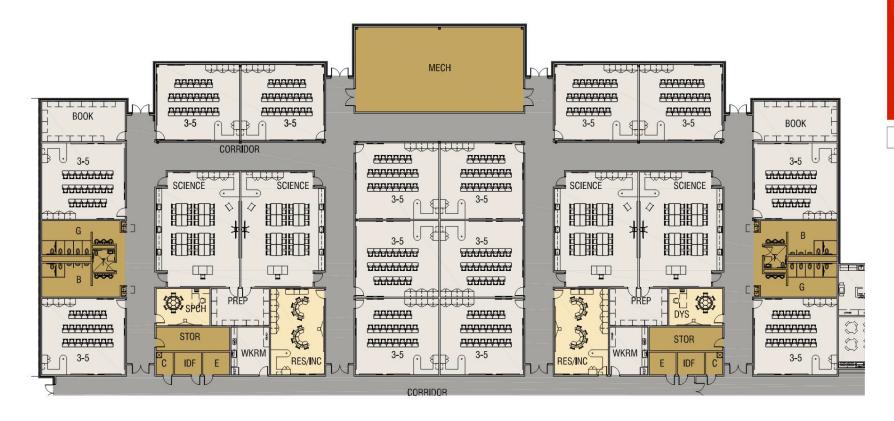
















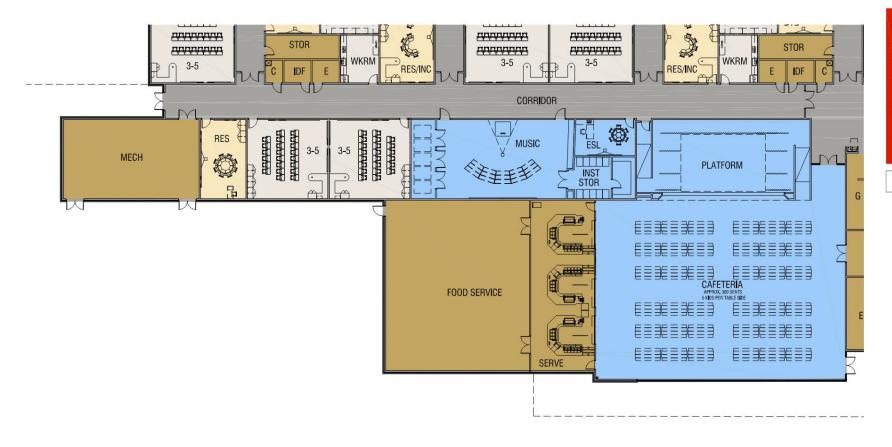

















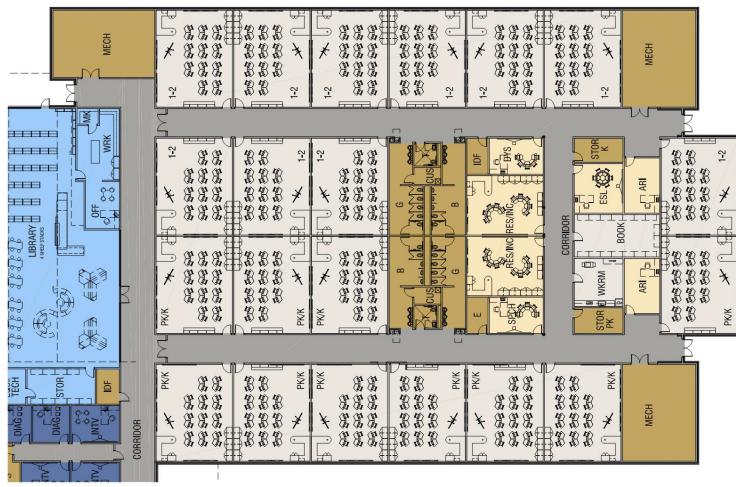







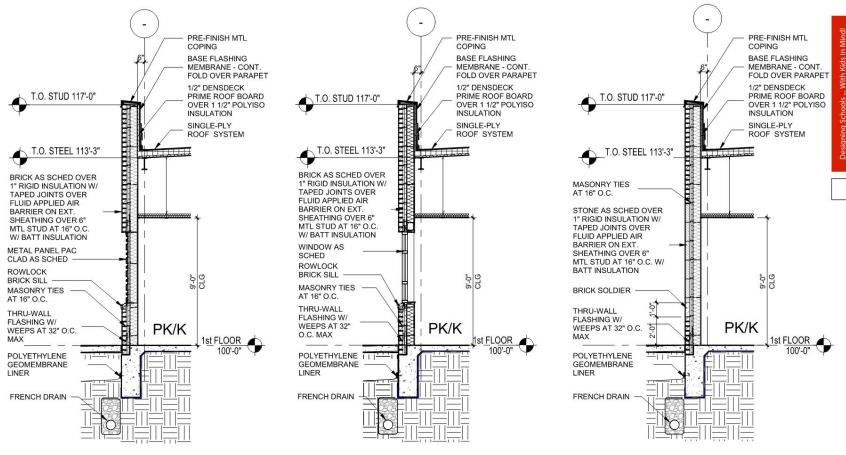




2 SECTION @ WINDOW SCALE: 1/4" = 1'-0"

1 SECTION @ STONE
SCALE: 1/4" = 1'-0"





WALL SECTIONS @ CLASSROOM 11/20/2024

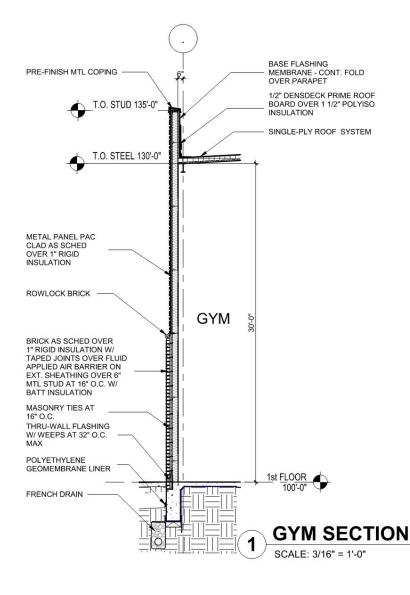



CLAYCOMB ASSOCIATES ARCHITECTS

WALL SECTIONS @ GYM














CARPET

WOOD PANELING



UTILITY BRICK







ACOUSTICAL FABRIC

MASONRY






PLASTIC LAMINATE






MATERIAL BOARD 11/20/2024













BUILDING ELEVATIONS 11.20.2024























































CONCEPTUAL RENDERING


























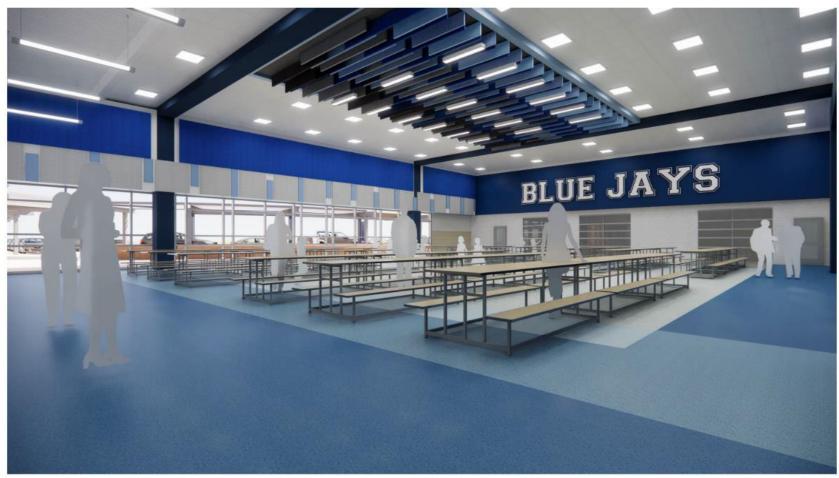
























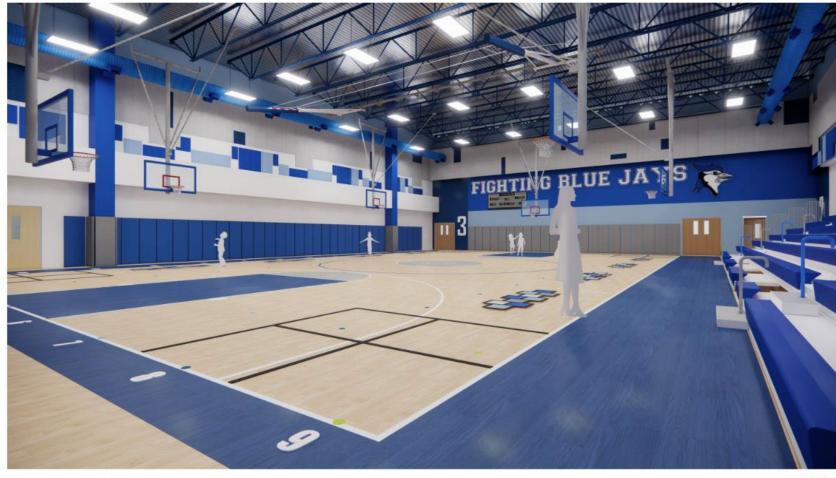






CONCEPTUAL RENDERING

11.20.2024

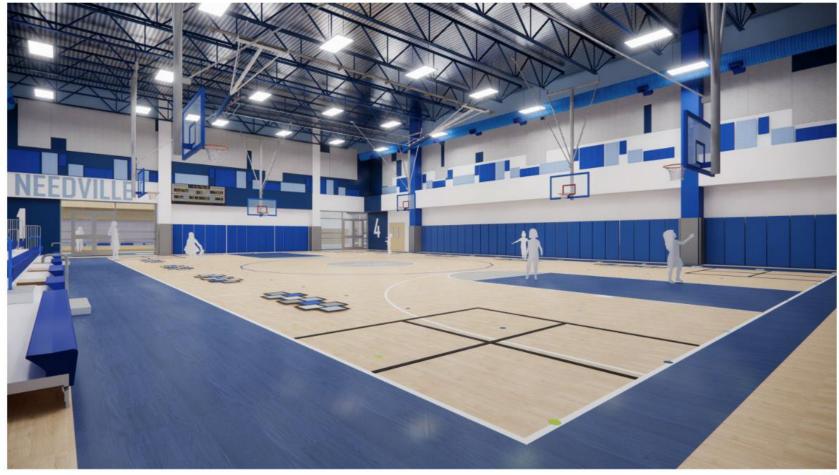

















							20	23			2024						2025						2026					2027								
					y 2023 rry 2023	2023	023	123	er 2023 or 2023	sber 2023 y 2024	rry 2024 2024	024	24	1 2024 riber 2024	rs 2024	y 2025	2025	520	25	nber 2025	2 2025 ober 2025	y 2026	rry 2026 2026	026 026	026	t 2026 riber 2026	er 2026 ober 2026	ber 2026	ry 2027	2027	027	12027	nber 2027 er 2027	iber 2027		
DUACE		•			Januar	March April 2	May 2 June 2	Augus Augus	Octob	Decen	Februs	April 2 Way 2	July 20	Septer	Noven	Januar	March Amil 2	May 2	John 20	Septer	Noven	Januar	Februa	April 2 May 2	June 2 July 20	Augus	Octob	Decer	Februs	April 2	May 2	Augus	Septer	Noven		
PHASE	Progress 100%	Start 1/1/2023	No. Days 536.0	End 6/20/2024	Н	**	**						$\mathbb{H}$	╫	╫	╫	Н	Н	$^{\rm H}$	H	Н					E:										Mind!
GEOTECH REPORT/SURVEY	50%	6/21/2024	45.0	8/5/2024	Н			+		Н			Н	╫	╫	₩	H	Н	₩	H	Н												&			Kids In
SCHEMATIC DESIGN	100%	5/29/2024	84.0	9/18/2024	Н	H	Н	H	H	H	H	Н		₩	╫	╫	H	H	H	H	H					10:										With
DESIGN DEVELOPMENT	100%	9/19/2024	28.0	11/20/2024	Н	H	Н	H	Ħ	H	H	Н		₩	╫	Ħ	Ħ	H	Ħ	Ħ	H												NS			schools
CONSTRUCTION DOCUMENTS (35% Review)	0%	11/22/2024	48.0	1/9/2025	Н	H	Н	Ħ	Ħ	H	H	Н	$\forall$	╫	₩	H	H	H	Ħ	Ħ	Н		A	IKE	: 51	JB.	JEC		U	CF	IAI	٧G	E	4		gning
CONSTRUCTION DOCUMENTS (65% Review)	0%	1/10/2025	34.0	2/13/2025	Н	H	Н	Ħ	Ħ	H	H	Н	$\forall$	╫	╫	₩	H	H	Ħ	Ħ	Ħ	Н	$\forall$	+	H	H	H	H	H	Ħ	Н	t	H	Н		Des
CONSTRUCTION DOCUMENTS (95% Review)	0%	2/14/2025	34.0	3/20/2025	H	H	Н	$\dagger \dagger$	$\dagger$	Ħ	H	H	$\forall$	╫	╫	100	H	Ħ	$\dagger\dagger$	$\dagger\dagger$	$\dagger\dagger$	$\dagger \dagger$	$\dagger \dagger$	$\dagger$	H	H	H	$\dagger$	Ħ	$\dagger \dagger$	$\dagger \dagger$	$\dagger$	$\dagger$	Н		
CONSTRUCTION DOCUMENTS (Bid Issue)	0%	3/21/2025	33.0	4/23/2025	H		Н	Ħ	Ħ	H	H	Н	$\forall$	₩	╫	Ħ	Ħ	Ħ	Ħ	Ħ	Ħ	Ħ	Ħ	T		H	H	Ħ	Ħ	Ħ	Ħ	t	$\dagger$	Ш		
BIDDING	0%	4/24/2025	28.0	5/22/2025	Ш	Ħ	Н	Ħ	Ħ	Ħ	Ħ	H	Ħ	₩	╫	Ħ	₩		Ħ	Ħ	Ħ	Ħ	Ħ	T	H	Ħ	Ħ	Ħ	Ħ	Ħ	Ħ	T	IT	Ш		
NEGOTIATIONS (ESTABLISH GMP)	0%	5/23/2025	33.0	6/25/2025	Ш	Ħ	П	Ħ	Ħ	Ħ	Ħ	П	Ħ	╫	⇈	Ħ	⇈	Ħ	Ħ	Ħ	Ħ	Ħ	Ħ	T	Ħ	IT	Ħ	Ħ	Ħ	Ħ	Ħ	T	ΙŤ	П	Ι.	
SCHOOL CONSTRUCTION	0%	6/26/2025	426.0	8/26/2026	П			Ħ		Ħ	П	П		₩	Ħ	Ħ	Ħ	Ħ	П	П	4	101	THS				П	П	П	Ħ	П		Ť	T		
PUNCH LIST	0%	8/27/2026	17.0	9/13/2026	Ш	25							-	╫	1		⇈	Ħ					-	0.0		ı	П	Ħ	Ħ	Ħ	Ħ			П		
SCHOOL YEAR BREAKS																																				
SPRING BREAK		March 13	4	March 17	Ш		П	П	П	П	П	П		#	#	П	#	Щ	П	П	П	П	П	П		1	П	П	П	П	П		I	П		
SUMMER BREAK FALL BREAK/SCHOOL HOLIDAY		May 24 November 21	73 4	August 5 November 25	Ш							Ш		₩	#	#	╫	╫		Ħ	1	H	$\parallel$			1		H	Ħ	$\sharp$	П			Ш		
WINTER BREAK		December 19	13	January 1	Ш		Ш	Щ	-l l-		Ц	Ш		Щ	Щ	11	#	щ		I.o.	Ш					L	Щ	Ш	Н	Н	Н		L	Ш		
					January 2023 February 2023	March 2023 April 2023	May 2023 June 2023	July 2023 August 2023	October 2023 Navember 2023	December 2023 January 2024	February 2024 March 2024	April 2024 May 2024	June 2024 July 2024	September 2024	October 2024 November 2024	January 2025 January 2025 Galerian 2025	March 2025	May 2025	July 2025	September 2025	Navember 2025	January 2026	February 2026 March 2026	April 2026 May 2026	June 2026 July 2026	August 2026 September 2026	October 2026 November 2026	December 2026	February 2027	March 2027 April 2027	May 2027 June 2027	July 2027 August 2027	September 202, October 2027	November 2027 December 2027		
							20	23				2	02	4				20	02!	5				2	02	6				- 2	20	27	, i			





### Needville ISD Code Adoptions

#### Sec. 14-19. – Codes adopted by reference:

- 2015 International Building Code
- 2015 International Fire Code
- 2012 International Fuel Gas Code
- 2012 International Mechanical Code
- 2015 International Plumbing Code
- 2012 International Property Maintenance Code
- 2015 International Existing Building Code
- 2015 International Energy and Conservation Code
- 2012 International Performance Code
- 2015 Residential Code for One and Two Family Dwellings
- 2017 National Electrical Code





### NEEDVILLE

INDEPENDENT SCHOOL DISTRICT

# WE APPRECIATE THE OPPORTUNITY TO SERVE YOU! THANK YOU!

